FGN WB NUC

THE 17 SECOND AFRICA HIGHER EDUCATION CENTRES OF EXCELLENCE FOR DEVELOPMENT IMPACT (ACE-IMPACT) PROJECTS

FINAL 2024 PROCUREMENT AUDIT REPORT

AFRICA CENTRE OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACE-SPED)

UNIVERSITY OF NIGERIA, NSUKKA ENUGU STATE

SUBMITTED BY

COSSET CONSULTANTS

KURIFTU PLAZA, SUITE C8, PLOT 519 OLU AWOTESU STREET, JABI DISTRICT, ABUJA, FCT.

TEL:+234(0)8033116002; +234(0)8123205980

EMAIL: COSSETCONSULTANTS@GMAIL.COM.

FEBRUARY 2025

CONTENT

S/NO	DESCRIPTION	PAGE NO.
1	TITLE PAGE	
2	TABLE OF CONTENTS	1
3	ABBREVIATIONS	3
4	**SECTION 1 - EXECUTIVE SUMMARY**	
	- General	4
	- Aim	4
	- Methodology and Review Procedure	4
	- General Contract Packages	5
	- Findings	8
	- Exit Meeting	11
	- Infractions	11
	- Procurement Process and Activities Assessment	10
	- Rating and Classification	13
	- Audit Opinion	13
	- Recommendation	14
5	**SECTION 2 - INTRODUCTION**	
	- Background	17
	- ACESPED UNN	17
	- NUC	18
	- WB Guideline	18
	- PPA, 2007	19
	- Procurement Audit of ACE-IMPACT	19
	- Engagement of Cosset Consultants	19
	- Objectives of Procurement Process Audit	19
	- Methodology	20
6	**SECTION 3 - SCOPE AND REVIEW SAMPLE**	
	- Audit Scope	22
	- Review Sample	22
7	**SECTION 4 - SPECIFIC CONTRACTS**	
	- Construction of ACESPED Service Core Building	25
	- Supply Of Laboratory Equipment: Back Scattered Electrons Analytical Equipment	28
	- Supply And Installation of Laboratory Equipment for Energy Dispersive Spectroscopy	31
	- Supply And Installation of Sub-System Components for The Mini-Grid to ACESPED Centre	34
	- Supply and Installation of Photovoltaic (PV) Panels	37

8	**SECTION 5 - APPENDICES**	
	- Appendix i – List of 2023 Procured contracts	41
	- Appendix ii – Checklists & Procurement Duration	44
	- Appendix iii – Exit Meeting Sheet	61
	- Appendix iv – Procurement Plan	81
	- Appendix v - Pictures	85
	- Appendix vi – Terms of Reference	89

ABBREVIATIONS AND ACRONYMSS

ACE	Africa Centre of Excellence.
ACE - IMPACT	Africa Centre of Excellence for Development Impact.
ACE-SPED	Africa Centre of Excellence for Sustainable Power and Energy Development.
CL	Centre Leader.
CQS	Consultant Qualification Selection.
DC	Direct contract.
FGN	Federal Government of Nigeria.
FME	Federal Ministry of Education.
GPN	General Procurement Notice.
IC	Individual Consultant.
ICB	International Competitive Bidding.
IDA	International Development Association.
IS	International Shopping.
LCS	Least Cost Selection.
LIB	Limited International Bidding.
M&E	Monitoring and Evaluation.
NAPCU	National ACE Project Coordination Unit.
NCB	National Competitive Bidding.
NGN	Nigerian Naira.
NPM	National Procurement Manual.
NS	National Shopping.
NUC	National Universities Commission.
NUS	National University System.
PAD	Project Appraisal Document.
PIU	Project Implementation Unit.
PM	Procurement Manual
PPA	Public Procurement Act
QCBS	Quality and Cost Based Selection
RFP	Request for Proposal
SBD	Standard Bidding Document
SPN	Specific Procurement Notice
SSS	Single Source Selection
STEM	Science, Technology, Engineering and Mathematics.
TA	Technical Assistance
TOR	Terms of Reference
UNN	University of Nigeria Nsukka.
USD	United States Dollar
VFM	Value for Money
WB	World Bank

SECTION 1 - EXECUTIVE SUMMARY

1.1 General

The National Universities Commission (NUC) appointed Cosset Consultants as consultants to carry out the Procurement Process Audit of the Africa Centre of Excellence for Sustainable Energy Development (ACE-SPED), University of Nigeria, Nsukka (UNN). UNN is one of the universities that are benefitting from the 17 Second Africa Higher Education Centres of Excellence for Development Impact (Ace-Impact) Projects.

1.2 Aim

The primary aim and objective of this Procurement Process Audit is to review the procurement, contracting and implementation processes and determine the extent to which laws guiding the procurement activities are complied with; and confirm their consistency with the ACE-Impact institutional guidelines and the World Bank general guiding principles. This audit also helps to identify non-compliances and deficiencies in the procurement activities and proffer appropriate corrective measures.

1.3 Methodology and Review Procedure

1.3.1 Methodology

The methodology and approach adopted for this post review are in three phases: (i) Inception activities (ii) Field works/activities (iii) Preparation and presentation of audit reports.

Generally, these phases include the determination of scope of assignment and selection of contracts to review. The study and evaluation of the Project/Contract files and other documents. Interactive meetings with the procurement staff. Data collection and analysis; physical site inspections; and the preparation of inception, draft and final procurement audit reports.

Data collection at the ACESPED was carried out with the use of checklists. Appendix II.

1.3.2 Review Procedure

The audit procurement procedure used at ACESPED is based on the institutional guidelines and it also considered the levels of compliances with the guidelines and the achievement of the Bank's procurement principles.

However, the procurement process activities of ACESPED are being implemented in consideration of section 15(1)a & b of the PPA 2007 Act as amended.

1.4 General Contract Packages

1. ACE-SPED procured twenty-four (24) contracts in 2024. Six (6) contracts are goods while eighteen (18) were works. There was no service as shown in appendix 1 - Inventory of sampled and reviewed contracts.

2. Three of the procurements that make up the twenty-four were paid for in United States Dollars (USD). The value is USD377,595.49. For the purpose of this exercise, these were converted to Naira at the rate of N891.10/$.

3. The appropriate procurement methods to use for every contract based on the threshold were also stated; alongside the methods used by the Centre. Appendix 1.

Table 1

VALUES OF GENERAL PROCUREMENT METHODS AND TYPES (AMOUNT/%)						
	METHOD			TYPE		
No	Method	Total Method Procured (N)	% of Procured Method	Type	Total Type Procured (N)	% of Procured Type
1	NCB	0.00	0.00	GOODS	478,419,628.62	40.00
2	RFQ	1,190,753,953.67	100.00	WORKS	712,334,325.05	60.00
3	TOTAL	1,190,753,953.67	100.00%	TOTAL	1,190,753,953.67	100.00%

1.4.1 General Procurement Methods

The procurement method used by the ACE-SPED was the Request for Quotation (RFQ). Figure 1. Table 1 above shows the values of the procurement methods.

Figure 1

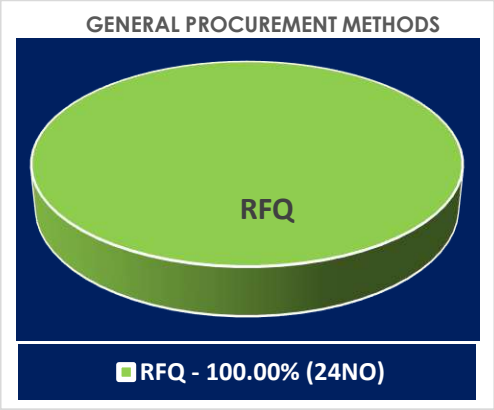

1.4.2 General Procurement Types

Goods appeared six (6) times on the 2024 procurement inventory at ACESPED. This represents 25% of the procurements. The remaining eighteen (18) procurement were works, representing 75% of the total procurements as illustrated on figure 2. Table 1 above shows the value representation of the procurement types.

Figure 2

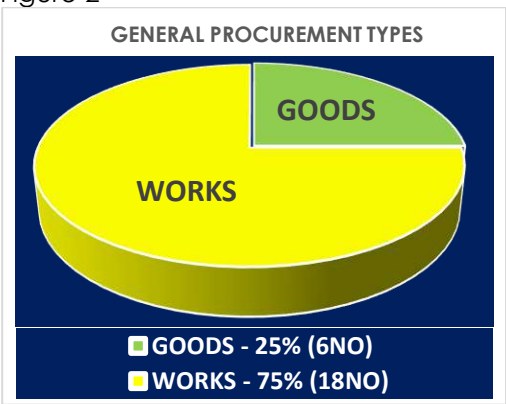

1.4.3 Sample Size

The audit sample size was eight (8) procurements, being 33.33% of the procurements in 2024. It was determined by random sampling of the procured items. The sample is made up of one (1) good and seven (7) works at about 12.50% and 87.50% respectively. RFQ was used for the eight (8) samples size. Tables 3 & 4.

TABLE 3 – FORM 3 - SELECTION OF REVIEW SAMPLE METHODS

	CONTRACTS	RFQ	NCB	SH	Total
		Post Review	Post Review	Post Review	Post Review
	Reviewed	8	0	0	8
		out of	out of	out of	out of
	Population	24	0	0	24

TABLE 4 – FORM 3 - SELECTION OF REVIEW SAMPLE TYPES

	CONTRACTS	Goods	Works	Services	Total
		Post Review	Post Review	Post Review	Post Review
	Reviewed	1	7	0	8
		out of	out of	out of	out of
	Population	6	18	0	24

Table 2

PROCURED/SAMPLE VALUES OF METHODS AND TYPES (AMOUNT/%)								
	METHOD				TYPE			
No	Method	Total Method Procured (N)	Reviewed Sample Method (N)	Review Sample (%)	Type	Total Type Procured (N)	Reviewed Sample Type (N)	Review Sample (%)
1	NCB	0.00	448,943,548.95	55.40	GOODS	478,419,628.62	361,542,956.00	44.60
2	RFQ	1,190,753,953.67	361,542,956.00	44.60	WORKS	712,334,325.05	448,943,548.95	55.40
3	TOTAL	**1,190,753,953.67**	**810,486,504.95**	**100.00%**	TOTAL	**1,190,753,953.67**	**810,486,504.95**	**100.00%**

1.4.3.1 Sample Method

The sample size of eight (8) contracts were all procured through the RFQ. Figure 3

Figure 3

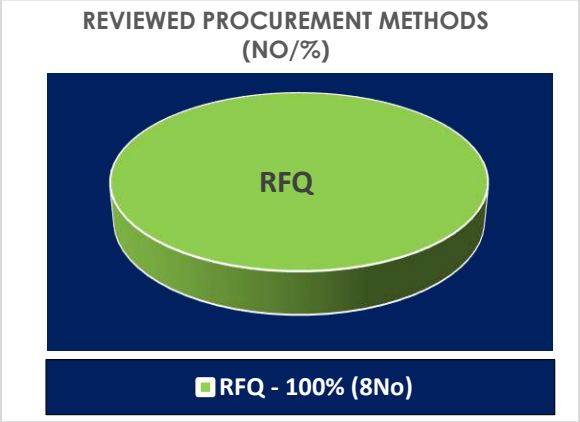

1.4.3.2 Sample Type

Seven (7) sampled procurements representing about 87.50% were goods contacts while One (1) was work at 12.50 % of sample. Figure 4.

Figure 4

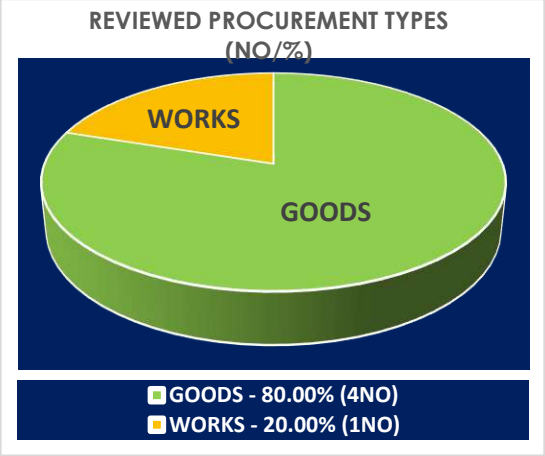

1.5 Findings

1. The ACE-SPED, University of Nigeria, Nsukka used the University's procurement guideline and the Public Procurement Act (2007) as amended in the 2024 procurement activities.

2. ACE-SPED presented a procurement list of twenty-four (24) procurements awarded from January 1, 2024 to December 31, 2024.

3. ACE-SPED obtained approval from the Bureau of Public Procurement (BPP) to use selective tendering for some of the contracts that are within the NCB thresholds.

4. The Center published most of its Request for Quotation (RFQ), on the school website.

5. The items procured are in the procurement plan.

6. The various approval boards and committees are well constituted and participated in the approval of the various contracts as presented by the procurement officer of the Centre. The various meetings were equally sighted. The examination and evaluation of tenders were moderate.

7. Standard Bidding Documents (SBD) were used for the procurements.

8. The ACE-SPED stated that most of the vendors that were invited to submit quotations were the ones that the university have used in the past, with commendable performances.

9. The Centre has qualified procurement staff, most of whose primary assignment are with the University's procurement department.

10. Prices were checked and found to be competitive.

11. Filling, storage and retrieval of procurement documents and information were not seamless.

12. Withholding Taxes (WHT) and Value Added Taxes (VAT) were

13. The unsuccessful bidders were not seen to have been notified of the award of the various contracts.

1.6 Exit Meeting

The exit meeting discussed te various identified issues in ACESPED's 2024 procurement activities. Explanations were given for certain actions toaken by the Centre towards these identified concerns. Advices were also given to the Centre on the need to ensure that the process continues to be managed well. The exit meeting data table is as in the attached appendix iii

1.7. Infractions

ACE-SPED were no infractions in consideration of the outcome of the meeting. ACEPED has no further explanations to make other than to ensure that subsequent procurement are issues free. The responses were satisfactory.

1.8 Procurement Process and Activities Assessment

The team considered the performance of the general procurement processes and activities at **ACEDHARS** to determine the level of exposure to perceived infractions and inconsistencies. The procurement activities were categorized into low, fair and good, with percentages ranges of 0-39.99%, 40-59.99% and 60-100% respectively.

Overall, the **ACE-SPED** has a **"MEDIUM"** risk grading and a **"GOOD"** procurement performance score.

1.9 Rating and Classification

The audit review opinion is classified and rated as shown on table 5 below

Table 5:

S/NO	GRADING (%)	CLASS	OPINION
1	75 - 100	Good	Satisfactory
2	50 – 74.99	Fair	Need Improvement
3	0 – 49.99	Poor	Unsatisfactory

1.10 Audit Opinion

ACESPED, University of Nigeria Nsukka is assessed to have earned a score of seventy percent (70%). The procurement process at the Centre **NEEDS IMPROVEMENT**. The opinion is considerably based on the implementation of the processes and the results of the activities with regards to the levels of compliances to the institutional guidelines, the Public Procurement Act 2007 and the general procurement principles.

Table 6 Performance and Compliant Grading

S/NO	ACTIVITY	BASIS	COMPLIANCE GRADE
1	Preparation of Procurement Plan	Based on WB Guideline	Good
2	Advertisements	Based on Institutional guideline and the PPA requirements	Good
3	Procurement Method	Based on Institutional guideline and the PPA requirements.	Fair
4	Bidding Processes	Based on Institutional guideline and the PPA requirements.	Good
5	Bid Evaluation & Reporting	Adherence to criteria	Good
6	Contract Award	Meeting awards requirements	Good
7	Documentations	Quality, filing, ease of retrieval and assessment	Fair
8	Competition and Equal opportunity	Based on WB Guideline	Good
9	Value for money (VFM)	Based on the PPA 2007 and WB requirements	Fair
10	Transparency	Based on WB Guideline	Fair
11	Economy	Based on Institutional guideline and the PPA 2007 and WB requirements.	Good
12	Efficiency	Based on the PPA 2007 and WB requirements.	Good
13	Contract Implementation, Monitoring and Evaluation	Based on Institutional guideline and the PPA requirements	Good

1.11 Recommendations

1. ACESPED should endeavor to observe thresholds to ensure that the appropriate procurement methods are used.

2. Agreements are very important documents in procurement contracts and the Centre should make it a priority to have one executed for every contract.

3. It is advised that copies of all documents relating to the centre's procurement activities be domiciled with the Centre. This is to allow seamless retrieval and provision of documents and information.

4. Unsuccessful bidders should always be debriefed. This makes them to be aware of their lapses and would help to create a healthier procurement environment through improved levels of competition, relationship and performance.

5. The performances of the reviewed contracts are detailed in the specific Contracts reviews below.

QS. Okoye N. Ifeanacho *FNIQS*
(Team Leader)
February 11, 2025

SECTION 2 – INTRODUCTION

2.1 BACKGROUND

Due to the need to promote regional specialization amongst Universities in the West and Central Africa sub-region within disciplines that address common regional challenges, the Africa Center of Excellence (ACE) Project aims at strengthening the capacities of these Universities to enable them deliver high quality training and applied research.

1. Africa Centre of Excellence (ACE 1) Project

The Africa Centre of Excellence (ACE 1) project was instituted in 2013 by the Government of Nigerian, Ghana, Benin Republic, Togo, Burkina Faso, Cameroun and Senegal with support from the World Bank.

The Federal Government of Nigeria (FGN) entered into a credit agreement (Credit Number 5415-NG) after securing US$70.0 million with the International Development Agency (IDA) of the World Bank (WB) to finance the ACEs project in 10 Nigerian Universities.

2. The Second Africa Higher Education Centres of Excellence for Development Impact (ACE- Impact) Project

The Second Africa Higher Education Centres of Excellence for Development Impact (ACE- Impact) Project resulted from the successes achieved with the ACE 1. ACE-Impact project has 43 Centres in the sub-region, with 17 of them being run by Nigeria Universities.

ACE-Impact project (Credit Number 6510-NG) was designed to inject $115 million to the Nigeria University System (NUS).

2.2 THE AFRICA CENTER OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT.

ACE-SPED stated its vision as "to establish a regional hub, focused on addressing the energy and power challenges of sub-Saharan Africa through research, education, and collaboration with sectoral partners".

Its objective is "to create a functional, problem-solving Center of Excellence with the capacity to impact meaningfully in power systems and energy development, through knowledge transfer and human capital upgrade".

2.3 NATIONAL UNIVERSITIES COMMISSION (NUC)

The **National Universities Commission (NUC)** of Nigeria is a parastatal under the Federal Ministry of Education (FME). It was established in 1962 as an advisory agency in the Cabinet Office and became a statutory body in 1974. NUC is a regulatory agency acting as a catalyst for positive change and innovation for the delivery of quality University education in Nigeria.

The **NUC** aims to: achieve a stable and crisis-free University System; upgrade and maintain physical facilities in the Nigerian University System for delivery of quality university education and match university graduate output with national manpower needs; work with Nigerian Universities to achieve full accreditation status for at least 80% of the academic programmes; foster partnership between the Nigerian University System and the private sector.

The National Coordination of the ACE projects is domiciled at the National Universities Commission (NUC). It is responsible for the National Project facilitation, training, and supervision in fiduciary aspects as well as national Monitoring and Evaluation (M&E) and minor Technical Assistance (TA) in Nigeria.

2.4 WORLD BANK PROCUREMENT GUIDELINE

The WB guideline has set rules guiding the procurement processes to be followed for procurement of good, works, consulting and non-consulting services being financed with loans from the WB. It covers the consideration of the WB core procurement principles in every contract.

Notwithstanding the established procurement guidelines, the FG/NUC and the WB have agreed to allow the ACE-Impact Centres to use the various institutions guidelines for the implementation of the projects.

2.5 PUBLIC PROCUREMENT ACT (PPA) 2007

The Public Procurement Act 2007 as amended guides all procurement activities of the Ministries Departments and Agencies (MDAs) in Nigeria. The PPA is regulated by the Bureau of Public Procurement (BPP). One of BPP's functions is to regulate and ensure the reduction of infractions, weaknesses and non-compliances aimed at reducing corruption in public procurement. It also aims to ensure value for money, economy, transparency, competition, fairness, integrity and accountability in public procurement activities; improved professionalism and enhanced service delivery.

The PPA Act 2007 as amended provides the basic guideline for the award and execution of contracts in Nigeria and promotes freedom of information that mandates all unclassified procurement records to be made available to appropriate public for inspection.

2.6 PROCUREMENT PROCESS AUDIT OF ACES

The purpose of the Procurement Audit of ACEs is to study, verify, interpret, and critically analyze all data, documents and Procurement statement collected/received and form true, fair and independent opinion on the Procurement Statements of the Procurement operation of ACE (Nigeria) for the period under review and to report findings to the National Universities Commission (NUC).

2.7 ENGAGEMENT OF COSSET CONSULTANTS

The NUC engaged Cosset Consultants to carry out post review of procurement activities of the 17 ACE-Impact Centres in fourteen (14) Nigeria Universities, including the ACE-SPED, University of Nigeria, Nsukka, Enugu State, Nigeria.

2.8 OBJECTIVES OF THE ACE-IMPACT PROJECT PROCUREMENT PROCESS AUDIT

This Procurement Audit is to identify and report on negligence in procurement management operations and decisions. It is also structured to bring to light all fraudulent acts, weaknesses, deficiencies and non-compliances that negatively affect procurement activities and recommend deterrents and corrective actions to ensure improved processes.

The Procurement audit gave objective assessments of the procedures specified in the Credit Agreement and determine the levels of compliances with institutional guidelines with respect to the considerations of the World Bank guiding principles.

2.9 METHODOLOGY

1. The methodology adopted for this assignment is generally concerned with investigations, inquiry, assertions, reasoning and research. The approach is objective, verifiable, and quantifiable. Interactions and interviews were held with officers of ACE-SPED that were involved in the various stages of the procurement process/activities. The opinions and clarifications from the ACE-SPED staff are considered and addressed in the report.

2. Contract data forms are used to collect the information that were analyzed. The contents of the form include information on general contracts, procurement and contracting, costs, time, contract administration, disbursement and deliverables. The documents made available to the consultant from which the data were collected include:

(1) Procurement Plan.
(2) Solicitation documents used before award.
(3) Contract files.
(4) Payment Vouchers.

3. Visits to selected project sites were undertaken to determine the quality of materials and labour deployed to the work by the contractor. It also helps to determine the level of supervision from the ACE-SPED procurement staff.

4. This data analyzed enabled the determination of the following critical success factors;

(1) Compliance with the provisions of the World Bank Procurement Guideline.

(2) Compliance with the provisions of the Public Procurement Act 2007 (examine the Management Control Framework in place to monitor procurement and contracting activities within ACE-SPED Project).

(3) Compliance with the use of standard bidding documents (examine procurement documents and contracts files issued between the stipulated periods).

(4) Compliance with the Code of Conduct for Public Officers involved in Procurement (review the processes undertaken by personnel of the ACE-SPED Project who are directly involved in procurement and contracting activities).

(5) Optimized commercial performance and value for money (review related procurement procedures, guidelines and processes and determine the level to which value for money was achieved).

5. Exit meeting was held with the procurement staff of the Centre. The observed key weaknesses and non-compliances were brought to their notice. The explanation given by the Centre staff are considered in the report.

6. The personnel interacted with at the ACE-SPED, UNN during the field works were:

(1) Deputy Centre leader.

(2) Director, Physical Planning Department

(3) Procurement Officer.

SECTION 3 – SCOPE AND REVIEW SAMPLES

3.1 AUDIT SCOPE

The procurement audit covers the review of all the procurement transactions, limited to the samples selected for audit, including prices reviews and compares of similar rates as at the time of award. Selected project site and inspection of procured goods, works and services are expected to be taken into consideration. The scope incudes determining the following:

1. Whether the procurement statements from the ACE-SPED procurement unit conform to accepted procurement principles in accordance with the NUC/WB guidelines.

2. Whether they fairly represent the financial position of the ACE-SPED project.

3 Whether the result of operations for a given period are accurately represented.

4. Whether the procurement statements have been altered.

3.2 REVIEW SAMPLE

During the field work, ACE-SPED presented their procurement plan with a list of twenty-four (24) procurements. In 2024.

Eight (8) procurements were selected for review. The selection was 33.33% of the procured contracts that is about 41.50% of the value of the total procurements in 2024.

The field work at the ACE-SPED was based on data sourced from available documents and information received from the ACE-SPED procurement unit.

Table 7– ANALYSIS OF COMPLETED/UNCOMPLETED CONTRACTS

S/NO		DESCRIPTION	NO OF PROJECTS COMPLETED	NO OF PROJECTS ON-GOING	TOTAL
1		January 1, 2024to December 31, 2024	24	0	24
		TOTAL	24	0	**24**

Table 8 – ANALYSIS OF COMPLETED/UNCOMPLETED CONTRACTS

S/NO	DESCRIPTION	PERCENTAGE
1	Completed	68.80%
2	Uncompleted	32.20%
	TOTAL	**100.00%**

Table 9 – ANALYSIS OF COMPLETED/UNCOMPLETED CONTRACTS

S/NO	DESCRIPTION	VALUE (N)	PERCENTAGE (%)
1	Completed	**1,190,753,953.67**	100.00
2	Uncompleted	0.00	0.00
	TOTAL	**1,190,753,953.67**	**100%**

This audit review was based on information extracted from the Center's Procurement Plan, as well as other documents made available to the Consultant by the ACE-SPED staff. There were also interviews and interactions with key personnel.

SECTION 4

SPECIFIC PROJECTS DETAILS

SECTION 4 - SPECIFIC CONTRACTS/PROJECTS DETAILS

4.1 CONSTRUCTION OF ACESPED SERVICE CORE BUILDING

4.1.1 Introduction

This contract was procured through National Competitive bidding (NCB). The award was made to **Messrs Faxco Nigeria Limited, No. 12 Kamba Street, Wuse Zone 2, Abuja**. with an award letter dated August 14, 2024 at a contract price of one hundred and sixteen million, five hundred and seventy -two thousand two hundred and forty-seven-naira, fifty kobo) N116,572,247.50 This is about USD73,325.10 at the exchange rate of USD 1,589.80 (August 14, 2024), and represent 0.08% of the Bank financing. The award was made to the lowest bidder.

The only payment seen to have been made to the contractor was the sum of N100,834,994.09 net with PV/2024/UNN-1/000000370 of September 6, 2024.

4.1.2 Observations/ Findings

The following are the major observations in the procurement process leading to the award of this contract.

4.1.2.1 Procurement Planning

This contract is in the 2024 procurement plan.

4.1.2.2 Advertisement

The contract was not advertised but the Centre obtain a no objection to use selection for the award.

4.1.2.3 Pre/Post Qualification

The contract amount is not within the threshold for prequalification.

4.1.2.4 Competition

There was quality competition in the process.

4.1.2.5 Bid Opening

The bids were opened publicly in the presence of the bidders, the Procurement Committee and some independent observers.

4.1.2.6 Bidding Documents

Standard bidding documents were used.

4.1.2.7 Evaluation of Bids/ Proposals

The bids were examined, evaluated and analysed by the bid evaluation committee. There was minute of meeting where the approval was granted by the University Tenders Board before award letter was issued to the successful bidder.

4.1.2.8 Award of Contract

Notification of award was issued to Messrs Faxco Nigeria Limited with an award letter dated August 14, 2024. The acceptance letter was made on August 23, 2024.

4.1.2.9 Contract Documents

Contract drawings, the Bills of Quantities, the Award letter, and the Acceptance letter form the contract document and they were all well executed. The Contract Agreement was not sighted.

4.1.2.10 Procurement Duration

The procurement processes leading up to the signing of contract was could not be ascertained because some of the dates were not sighted.

4.1.2.11 Contract Implementation

The project is ongoing and the quality in terms of the materials and labour is commendable. The project supervision was progressing satisfactorily.

4.1.2.12 Payments

The contractor did not request for mobilization. The only payment seen to have been made on the contract as at the date of audit on February 6, 2025 was the sum of net sum of N100,834,994.09 with PV/2024/UNN-1/000000370 of September 6, 2024.

4.1.2.13 Physical Inspection

The project was not inspected.

4.1.3 Recommendation

Based on the procurement audit process field work at the ACESPED, this project execution is commendable.

4.1.4 Conclusion

In view of the above observations and recommendations, ACE-SPED should continue with adhering to the rules, regulations and principles guiding the Public Procurement Process, ensuring that relevant documents are provided seamlessly.

4.2 SUPPLY OF LABORATORY EQUIPMENT: BACK SCATTERED ELECTRONS ANALYTICAL EQUIPMENT – LOT 3

4.2.1 Introduction

The procurement process of this contract was initiated with a letter from ACESPED to the BPP requesting for a "No Objection" approval to use selective tendering instead to procure the goods. ACESPED cited inadequate time to use NCB as the World Bank team was expected to commission the equipment on their arrival in November, 2023. The BPP gave approval to ACESPED and stressed that all bidders should have Original Equipment Manufacturers (OEM) Authorization.

ACESPED conducted the procurement process and bids were completed and returned. The Procurement Committee (PC) opened the bids in the presence of the bidders and some independent observers. Bids examinations and evaluation were carried out and the PC made recommendation for award to be made to **Messrs Katchey Company Ltd, of 28632 Roadside Drive Suite 230 Agoura Hills, California, 91301, USA** in the sum of USD128,216.36. This is about 2.14% of the Bank financing. The award letter is dated January 23, 2024. As at the date of audit on February 23, 2023, no payment was presented as having been made to the supplier. No goods have been supplied as well.

4.2.2 Observations/ Findings

Other observations regarding this procurement are as stated below:

4.2.2.1 Procurement Planning

The procurement was in the signed 2024 Procurement Plan.

4.2.2.2 Advertisement

There was no advertisement. Quotations were requested from selected vendors in line with the BPP approval to use selective tendering to procure the contract.

4.2.2.3 Pre/Post Qualification

Prequalification was not caried out, but consideration was mainly on who had authorization of the OEM.

4.2.2.4 Competition

There was relative competition as evaluation of the four (4) bidders indicated.

4.2.2.5 Bid Opening

Bids were opened by the PC at the close of submission in the presence of the bidders, and some independent observers.

4.2.2.6 Bidding Documents

Standard Bidding Documents SBD) were used during the process.

4.2.2.7 Evaluation of Bids/ Proposals

Bid evaluation report saw the PC recommending award to be made to Messrs Katchey Company Ltd. All bidders had OEM authorization.

4.2.2.8 Awards of Contract

The award letter dated January 23, 2024 was issued to Messrs Katchey Company Ltd in the sum of USD128,216.36. The acceptance of award of contract was made through the letter dated January 25, 2024.

4.2.2.9 Contract Documents

The contract agreement was not sighted. However, the quotation, the award letter, and the acceptance letter constitute the contract document.

4.2.2.10 Contract Implementation

The goods were supplied and installed with no price variation.

4.2.2.11 Payments

Evidence and amount of payment was not sighted.

4.2.2.12 Physical Inspection

There was no inspection.

4.2.3 Recommendation

1. The Centre must make it a point of duty to ensure that agreements are entered into with contractors on every

contract. Where such was done, the Centre should provide the evidence when requested.

2. Documents should be supplied seamlessly.

4.2.4 Conclusion

The procurement process is commendable.

4.4 LANDSCAPING AND EXTERNAL WORKS TO ACE-SPED CORE ADMINISTRATIVE BUILDING PREMISES (PERIMETER FENCING LOT 1) AT UNIVERSITY OF NIGERIA, NSUKKA CAMPUS

4.4.1 Introduction

This contract is in the 2024 procurement plan of the center and was procured using Request for Quotation (RFQ) instead of National Competitive Bid (NCB) method considering the threshold. The procurement processes started with an invitation to bid sent to three contractors on July 12, 2024 with a deadline for submission on August 2, 2024 and the three contractors submitted their quotations before the deadline. Messrs. Bethlyke Nigeria limited bided N49,257,790.00, Messrs. Saint Engineering bided N55,532,457.50 and Messrs. Amah Technical & Universal Contractors Ltd. bided N58,665,007.50. The bids were evaluated and analyzed on August 7, 2024.

Following the Bid evaluation, a recommendation of award to Messrs. Bethlyke Nigeria limited was made to the Tender's Board for approval as the bidder with the most competitive bid. A notification of contract Award was issued to **Messrs. Bethlyke Nigeria limited whose business is located at 79 Ogui Road, Enugu, Enugu State** and the contractor accepted with an acceptance letter dated August 23, 2024. The contract was valued at Forty-Nine Million, Two Hundred and Fifty-Seven Thousand, Seven Hundred and Ninety Naira (N49,257,790.00), having a Dollar equivalence of Thirty Thousand, Nine Hundred and Eighty-three Dollar, Sixty-Four Cents ($30,983.64) based on an Exchange rate of One thousand, Five Hundred and Eighty-Nine Naira, Eighty Kobo (N1,589.80/$1) per Dollar as at August 14, 2024 accounting for 0.52% of the total Bank's financing.

The contract duration was supposed to last for Four (4) weeks, but the contractor completed it with two weeks and a request for payment Certificate No. 1 (Final) was made on August 27, 2024. This request was approved on August 29, 2024 and a net payment of Forty-Two Million, Six Hundred and Seven Thousand, Nine Hundred and Eighty-Eight Naira, Thirty-Five Kobo (N42,607,988.35 Net) - Being Payment for Landscaping and External Works at ACE-SPED Administrative was made through a Payment Voucher No. PV/2024/UNN-1/000000334 of September 2, 2024.

4.4.2 Observations/ Findings

The review showed the following observation regarding the process;

4.3.2.1 Procurement Planning

This contract is in the ACE-SPED 2024 procurement plan.

4.3.2.2 Advertisement

There was no Advertisements.

4.3.2.3 Pre/Post Qualification

Pre-Qualification exercise does not apply to this procurement.

4.3.2.4 Competition

There was considerable competition with the process.

4.3.2.5 Bid Opening

Bid opening was done

4.3.2.6 Bidding Documents

Standard bidding documents were used for this contract

4.3.2.7 Evaluation of Bids/ Proposals

Bid evaluation was done on August 7, 2024

4.3.2.8 Award of Contract

The contract was awarded to Messrs. Bethlyke Nigeria limited at a contract value of N49,257,790.00

4.3.2.9 Contract Documents

The Quotations, Award and Acceptance letters constitute the contract documents.

4.3.2.10 Procurement Duration

The procurement duration took a total of 38 Days from the date of invitation to Bid to the date of contract Award.

4.3.2.11 Contract Implementation

The contract implementation was moderate considering the timeline for delivery.

4.3.2.12 Payments

N42,607,988.35 Net - Payment for Landscaping and External Works at ACE-SPED Administrative through a Payment Voucher No. PV/2024/UNN-1/000000334 of September 2, 2024.

4.3.2.13 Physical Inspection

There was no physical inspection.

4.3.3 Recommendation

Based on the audit process field work at the ACE-SPED the following recommendations are made:

Though the project allowed Institutions to use their guideline, it should be practiced with caution.

4.3.4 Conclusion

The procurement process for this contract had some lapses especially with documentations.

4.4 LANDSCAPING AND EXTERNAL WORKS TO ACE-SPED CORE ADMINISTRATIVE BUILDING PREMISES (DRAINS, KERBS AND GRASSING) LOT 3 AT UNIVERSITY OF NIGERIA, NSUKKA CAMPUS

4.4.1 Introduction

This contract is in the 2024 procurement plan of the Center and, it was procured using the Request for Quotation (RFQ) method. The procurement processes began with a letter of invitation to tender issued to three compliant contractors on July 12, 2024 with a deadline for submission on August 2, 2024. The three contractors submitted their quotations before the deadline. Messrs. Bethlyke Nigeria limited bided N35,168,678.75, Messrs. Faxco Nigeria limited bided N33,995,585.00 and Messrs. MCO Contractors bided N30,556,552.50. The bids were evaluated and analyzed on August 7, 2024 and a recommendation of award to Messrs. MCO Contractors as the bidder with the most competitive bid was made.

A notification of contract award was issued to **Messrs. MCO Contractors of 12 Nza Street, Independence Layout, Enugu, Enugu State.** The contract Award was accepted by the contractor with an acceptance letter dated August 23, 2024 at a contract value of Thirty Million, Five Hundred and Fifty-Six Thousand, Five Hundred and Fifty-Two Naira, Fifty Kobo (N30,556,552.50) which is equivalent to Nineteen thousand, Two Hundred and Twenty Dollar, Thirty-Eight Cents ($19,220.38) calculated using an exchange the rate of One thousand, Five Hundred and Eighty-Nine Naira, Eighty Kobo (N1,589.80/$1) per Dollar as at August 14, 2024 representing 0.32% of the total Bank financing.

The contractor completed the project and requested for payment Certificate No. 1 (Final) on August 27, 2024. This request was approved on August 29, 2024 and a Net payment of Twenty-Six Million, Four Hundred and Thirty-One Thousand, Four Hundred and Seventeen Naira, Ninety-One Kobo (N26,431,417.91 Net) - Being Payment for Landscaping and External Works at ACE-SPED through a Payment Voucher No. PV/2024/UNN-1/000000395 of September 2, 2024.

4.4.2 Observations/ Findings

The review showed the following observation regarding the process;

4.4.2.1 Procurement Planning

This contract is in the ACE- SPED 2024 procurement plan.

4.4.2.2 Advertisement

It was not advertisements.

4.4.2.3 Pre/Post Qualification

Pre-Qualification exercise does not apply to this procurement.

4.4.2.4 Competition

There was a considerable competition with the process.

4.4.2.5 Bid Opening

Bid opening was done

4.4.2.6 Bidding Documents

Standard bidding documents were used for this contract

4.4.2.7 Evaluation of Bids/ Proposals

Bid evaluation was done on August 7, 2024

4.4.2.8 Award of Contract

The contract was awarded to Messrs. MCO Contractors at a contract value of N30,556,552.50

4.4.2.9 Contract Documents

The Quotations, award and acceptance letters constitute the contract documents.

4.4.2.10 Procurement Duration

The procurement duration took a total of 38 Days from the date of invitation to Bid to the date of contract Award.

4.4.2.11 Contract Implementation

The contract implementation was moderate considering the timeline for delivery.

4.4.2.12 Payments

N26,431,417.91 Net - Payment for Landscaping and External Works at ACE-SPED through a Payment Voucher No. PV/2024/UNN-1/000000395 of September 2, 2024.

4.4.2.13 Physical Inspection

There was no physical inspection

4.4.3 Recommendation

Based on the audit process field work at the ACE-SPED the following recommendations are made:

Though the project allowed Institutions to use their guideline, it should be practiced with caution.

4.4.4 Conclusion

The procurement process for this contract had some lapses especially with documentations.

4.5 PROPOSED CONSTRUCTION OF GENERATOR HOUSE AND PROCUREMENT OF 200KVA GENERATOR FOR ACE-SPED CORE BUILDING UNIVERSITY OF NIGERIA, NSUKKA CAMPUS

4.5.1 Introduction

This contract is in the 2024 procurement plan of the Center and, it was procured using the Request for Quotation (RFQ) method. The procurement processes commenced with a letter dated September 3, 2024 requesting for quotation from three contractors who had all the necessary mandatory compliant documents for seeking Government contracts for 2024 Fiscal year. These contractors submitted their quotations before the September 29, 2024 deadline. Messrs. Fraemmanon Investment quoted N60,381,184.80, Messrs. Livingspring Techical and Co. quoted N61,273,860.50 and. quoted and Messrs. Slott Nigeria Limited quoted N61,660,925.00.

Twenty-Six (26) Days later, the bids were evaluated and analyzed to ascertain the most competitive bids of all, and Messrs. Fraemmanon Investment became the winner. The contract Awarded was issued to **Messrs. Fraemmanon Investment whose business is located at 3rd Floor, 4 Ogui Road, Enugu, Enugu State**, on October 30, 2024 which was valued at Sixty Million, Three Hundred and Eighty-One Thousand, One Hundred and Eighty-Four Naira, Eighty Kobo (N60,381,184.80). The contractor accepted the contract Award the next day being October 31, 2024 with an Acceptance letter stating his commitment in carrying out the contract in conformity with standard. This contract value can equivalent to Thirty-Five Thousand, One Hundred and Sixty Dollar, Fifty-Three Cents ($35,160.53) as the Dollar equivalent calculated using an Exchange rate of One Thousand, Seven Hundred and Seventeen Naira, Thirty Kobo (N1,717.30/$1) per Dollar as at October 30, 2024, representing 0.59% of the total Bank financing.

On November 8, 2024, the contractor completed the contract and requested for payment Certificate No. 1 (Final) which equivalent to the contract sum. This request was approved the same day and a

Net payment of Fifty-Two Million, Two Hundred and Twenty-Nine Thousand, Seven Hundred and Twenty-Four Naira, Eighty-Five Kobo (N52,229,724.85 Net) – being PMT for construction of Generator House and Procurement of 200KV was made through a Payment Voucher No. PV/2024/UNN-1/000000463 of November 11, 2024.

4.5.2 Observations/ Findings

The review showed the following observation regarding the process;

4.5.2.1 Procurement Planning

This contract is in the ACE- SPED 2024 procurement plan.

4.5.2.2 Advertisement

It was not advertised.

4.5.2.3 Pre/Post Qualification

Pre-Qualification exercise does not apply to this procurement.

4.5.2.4 Competition

There was a considerable competition with the process.

4.5.2.5 Bid Opening

Bid opening was done

4.5.2.6 Bidding Documents

Standard bidding documents were used for this contract

4.5.2.7 Evaluation of Bids/ Proposals

Bid evaluation was done on October 27, 2024

4.5.2.8 Award of Contract

The contract was awarded to Messrs. Fraemmanon Investment at a contract value of N60,381,184.80

4.5.2.9 Contract Documents

The Quotations, Award and Acceptance letters constitute the contract documents.

4.5.2.10 Procurement Duration

The procurement duration took a total of 57 Days from the date of invitation to Bid to the date of contract Award.

4.5.2.11 Contract Implementation

The contract implementation was moderate considering the timeline for delivery.

4.5.2.12 Payments

N52,229,724.85Net – PMT for construction of Generator House and Procurement of 200KV through a Payment Voucher No. PV/2024/UNN-1/000000463 of November 11, 2024.

4.5.2.13 Physical Inspection

There was no physical inspection

4.5.3 Recommendation

Based on the audit process field work at the ACE-SPED the following recommendations are made:

Though the project allowed Institutions to use their guideline, it should be practiced with caution.

4.5.4 Conclusion

The procurement process for this contract had some lapses especially with documentations.

4.6. DRILLING OF BOREHOLE FOR WATER RETICULATION AT THE CORE BUILDING ACE-SPED CENTRE, UNIVERSITY OF NIGERIA NSUKKA CAMPUS

4.6.1 Introduction

This contract was included in the procurement plan of the Centre for the year 2024 and was procured using request for quotation (RFQ). The letter requesting for quotations was sent to three (3) vendors on April 30, 2024 with May 21, 2024 as the date for submission. Three (3) vendors submitted quotation for this contract in response to the request letter and the details of the quotations are as follows; Messrs. Faxco Nigeria Limited quoted N19,984,575.00 with a completion period of eight (8) weeks, Messrs. Saint Engineering Nigeria Limited quoted N21,000,000.00 with a completion period of ten (10) weeks and Messrs. Bonez Nigeria Limited quoted N23,200,825.00 with a completion period of ten (10) weeks. Recommendations were made after evaluation and a report was released on May 23, 2024. Following this, the contract was awarded to Messrs. Faxco Nigeria Limited, with a contract sum of Nineteen Million, Nine Hundred and Eighty-Four Thousand, Five Hundred and Seventy-Five Naira(N19,984,575.00) which is the Dollar equivalent of Thirteen Thousand, Four Hundred and Forty Dollars, Forty-Two cents (USD 13,440.42) exchanged at the rate of One Thousand, Four Hundred and Eighty-Six Naira, Ninety Kobo per Dollar (N1,486.90/$1) representing 0.22% of the Bank's financing. The letter of acceptance from the contractor and the signed contract agreement were not sighted. Following the successful completion of the contract, a net sum of N16,754,840.55 was paid for the drilling of borehole for water reticulation at the core building ACE-SPED Centre, University of Nigeria Nsukka campus through voucher no.: PV/2024/UNN-1/000000285 on June 8, 2024.

4.6.2 Observations/ Findings

The following observation in respect to the process were made during the review;

4.6.3 Procurement Planning

The contract was included in the procurement plan of the Centre.

4.6.2.2 Advertisement

Advertisement was not carried out.

4.6.2.3 Pre/Post Qualification

Separate Pre-Qualification exercise does not apply to this procurement process.

4.6.2.4 Competition

There was a considerable level of competition with the process as three (3) vendors submitted quotations for this contract.

4.6.2.5 Bid Opening

Bid opening date was not sighted.

4.6.2.6 Bidding Documents

Standard bidding documents were not used for this procurement process.

4.6.2.7 Evaluation of Bids/ Proposals

Bid evaluation report was dated May 23, 2024.

4.6.2.8 Award of Contract

The contract was awarded to MESSRS. FAXCO NIGERIA LIMITED on June 6, 2024.

4.6.2.9 Contract Documents

The constituents of this contract documents include; the letter of award. The acceptance letter, signed contract agreement and SBDs were not sighted.

4.6.2.10 Procurement Duration

The procurement duration for this contract took a period of 34 Days from the solicitation period to the date of contract award.

4.6.2.11 Contract Implementation

The contract implementation for this contract was fair taking into consideration the procurement method used and outcome of the process.

4.6.2.12 Payments

N16,754,840.55 – being net payment drilling of borehole for water reticulation at the core building ace-sped Centre, University of Nigeria Nsukka campus through voucher no.: PV/2024/UNN-1/000000285 on June 8, 2024.

4.6.2.13 Physical Inspection

The audit team did not make physical inspection of the goods.

4.6.3 Recommendation

i. The Centre should prioritize the safe keeping of all relevant documents regarding any contract for audit purposes as references can be made to them.

4.6.4 Conclusion

The center must continue to adhere to the standard procedures as they apply to all contracts in accordance with their thresholds. This is to ensure that there is complete competition and transparency.

APPENDICES

APPENDIX 1
LIST OF PROCUREMENTS BY ACE-SPED

UNIVERSITY OF NIGERIA NSUKKA, ENUGU STATE – ACE-SPED

APPENDIX 1 -INVENTORY OF PROCURED ITEMS/SAMPLED & REVIEWED PROJECT

S/NO	PACKAGE NO	DESCRIPTION	CONTRACTOR/ BENEFICIARY	AMOUNT		DATE	TYPE	METHOD USED	APPROPRIATE METHOD	REVIEWED CONTRACTS	REMARKS
				(NAIRA)	(DOLLAR)						
		UNN - ACE-SPED									
		GOODS									
1		**XRF SPECTROMETER - AIR & HELIUM LABORATORY EQUIPMENT - LOT 1**	**MESSRS. KATCHEY COMPANY LIMITED**	**114,253,598.39**	**128,216.36**	**JANUARY 23. 2024**	**GOODS**	**DC**		**REVIEWED**	**COMPLETED**
2		MAUD (MATERIAL ANALYSIS USING DIFFRACTION SOFT) LABORATORY EQUIPMENT - LOT 2	MESSRS. KATCHEY COMPANY LIMITED	109,108,903.83	122,442.94	JANUARY 23. 2024	GOODS	DC			COMPLETED
3		SSRT, REFLECTIVE AND TRANSMISSION SYSTEM LABORATORY EQUIPMENT - LOT3	MESSRS. KATCHEY COMPANY LIMITED	113,112,838.90	126,936.19	JANUARY 23. 2024	GOODS	DC			COMPLETED
4		TOYOTA HIACE BUS	MESSRS KOJO MOTORS LTD	99,750,000.00	N/A	MARCH 1. 2024	GOODS	RFQ	RFQ		COMPLTED
5		SUPPLY AND INSTALLATION OF OF AIR CONDITIONERS TO ACESPED CORE BUILDING	MESSRS. BETHIYKE NIGERIA LIMITED	28,906,750.00	N/A	OCTOBER 30. 2024	GOODS	RFQ	RFQ		COMPLETED

6		SUPPLY AND INSTALLATION OF CCTV CAMERAS TO ACESPED CORE BUILDING	MESSRS. FRAEMMANON INVESTMENT LIMITED	13,287,537.50	N/A	OCTOBER 30. 2024	GOODS	RFQ	RFQ		COMPLETED
		WORKS									
7		EXTERNAL WORKS TO MINI-GRID LAB SITE	MESSRS. ZIK-ON ENGINEERING SERVICES	8,656,975.00	N/A	MAY 8. 2024	WORKS	RFQ	RFQ		COMPLETED
8		LOT 2 - FURNISHING OF ACESPED CORE BUILDING PREMISES	MESSRS. UZ INVESTMENT LTD	19,296,250.00	N/A	JUNE 3. 2024	WORKS	RFQ	RFQ		COMPLETED
9		LOT 3 - FURNISHING OF ACESPED CORE BUILDING PREMISES	MESSRS. UZ INVESTMENT LTD	19,989,625.00	N/A	JUNE 3. 2024	WORKS	RFQ	RFQ		COMPLETED
10		LOT 4 - FURNISHING OF ACESPED CORE BUILDING PREMISES	MESSRS. UZ INVESTMENT LTD	19,763,875.00	N/A	JUNE 3. 2024	WORKS	RFQ	RFQ		COMPLETED
11		**DRILLING OF BORE HOLE AT CORE BUILDING**	**MESSRS. FAXCO NIGERIA LTD**	**19,984,575.00**	**N/A**	**JUNE 3. 2024**	**WORKS**	**RFQ**	**RFQ**	**REVIEWED**	**COMPLETED**
12		ELEVATED STEEL TANK & 4 NOS GEEPEE TANK AND ASSOCIATED PIPE WORK AT CORE BUILDING	MESSRS. BETHIYKE NIGERIA LTD	12,556,500.00	N/A	JUNE 3. 2024	WORKS	RFQ	RFQ		COMPLETED
13		LOT 6 - FURNISHING OF ACESPED CORE BUILDING (FIRST FLOOR OFFICE FURNITURE)	MESSRS. LIVING SPRING TECHNICAL & COY	19,886,425.00	N/A	AUGUST 14. 2024	WORKS	RFQ	RFQ		COMPLETED
14		**LOT 1 - LANDSCAPING & EXTERNAL WORKS TO CORE BUILDING (PERIMETER FENCING)**	**MESSRS BETHIYKE NIGERIA LIMITED**	**49,257,790.00**	**N/A**	**AUGUST 14. 2024**	**WORKS**	**DC**	**NCB**	**REVIEWED**	**COMPLETED**

15		**LOT 2 - LANDSCAPING AND EXTERNAL WORKS TO CORE BUILDING (DRIVES AND PARKS)**	**MESSRS FAXCO NIGERIA LIMITED**	**116,572,247.50**	**N/A**	**AUGUST 14. 2024**	**WORKS**	**DC**	**NCB**	**REVIEWED**	**COMPLETED**
16		**LOT 3 - LANDSCAPING & EXTERNAL WORKS TO CORE BUILDING (DRAINS, KERBS AND GRASSING)**	**MESSRS MCO CONTRACTORS**	**30,556,552.50**	**N/A**	**AUGUST 14. 2024**	**WORKS**	**RFQ**	**NCB**	**REVIEWED**	**COMPLETED**
17		Lot 5 - FURNISHING OF ACESPED CORE ADMINISTRATIVE BUILDING (FIRST FLOOR LECTURE HALL SEATS)	MESSRS. LIVING SPRING TECHNICAL & COY	19,791,287.50	N/A	AUGUST 14. 2024	WORKS	RFQ	RFQ		COMPLETED
18		Lot 1 - FURNISHING OF ACESPED CORE ADMINISTRATIVE BUILDING (GROUND FLOOR OFFICE FURNITURE)	MESSRS. LIVING SPRING TECHNICAL & COY	19,629,500.00	N/A	AUGUST 14. 2024	WORKS	RFQ	RFQ		COMPLETED
19		CONSTRUCTION OF GATE HOUSE AND STEEL GATE FOR ACESPED CORE BUILDING	MESSRS. FAXCO NIGERIA LIMITED	48,364,540.25	N/A	OCTOBER 30. 2024	WORKS	RFQ	NCB		COMPLETED
20		**CONSTRUCTION OF GENERATOR HOUSE AND PROCUREMENT OF 200 KVA GENERATOR FOR ACESPED CORE BUILDING**	**MESSRS. FRAEMMANON INVESTMENT LIMITED**	**60,381,184.80**	**N/A**	**OCTOBER 30. 2024**	**WORKS**	**RFQ**	**NCB**	**REVIEWED**	**COMPLETED**

21		FABRICATION AND INSTALLATION OF HOSTEL FURNITURE TO SCHOLARS VILLAGE (22 ROOMS) FOR USE BY ACESPED STUDENTS	MESSRS. SLOTTS NIGERIA LIMITED	49,170,500.00	N/A	OCTOBER 30. 2024	WORKS	RFQ	NCB		COMPLETED
22		**SUPPLY AND INSTALLATION OF 500 KVA TRANSFORMER AND ASSOCIATED INSTALLATION ACCESSORIES TO ACESPED CORE BUILDING**	**MESSRS. ORBNEST SYSTEMS**	**65,647,562.50**	**N/A**	**OCTOBER 30. 2024**	**WORKS**	**RFQ**	**NCB**	**REVIEWED**	**COMPLETED**
23		FABRICATION AND INSTALLATION OF OFFICE FURNITURE TO ACESPED CORE BUILDING FIRST AND SECOND FLOOR (LOT 1)	MESSRS. SLOTTS NIGERIA LIMITED	95,313,800.00	N/A	OCTOBER 30. 2024	WORKS	RFQ	NCB		COMPLETED
24		**FABRICATION AND INSTALLATION OF LECTURE HALL SEATS TO ACESPED CORE BUILDING FIRST AND SECOND FLOOR (LOT 2)**	**MESSRS. LIVING SPRING TECHNICAL & COY**	**37,515,135.00**	**N/A**	**OCTOBER 30. 2024**	**WORKS**	**RFQ**	**NCB**	**REVIEWED**	**COMPLETED**
				1,190,753,953.67	**377,595.49**					**33.33% REVIEW SAMPLE**	

APPENDIX II
CHECKLIST AND PROCUREMENT DURATION FORMS

AFRICA CENTRE OF EXCELLENCE CENTRE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA

GOOD

CHECK LIST

1. SUPPLY OF LABORATORY EQUIPMENT:XRF SPECTROMETER-AIR & HELIUM INCLUDING INSTALLATION/COMMISSIONING/END USER TRAINING (LOT 1) TO ACESPED BUILDING

LOAN/CREDIT NO. 6510-NG	**REVIEW DATE:** FEBRUARY 12, 2025			
CONTRACT DATA				
Contract Name & Number: Supply of Laboratory Equipment:XRF Spectrometer-AIR & Helium including installation/commissioning/end user training (Lot 1) to ACESPED Building	**Type of Contract: Lump Sum**			**Contract Amount: USD**
	Goods (**X**)	Works ( )	Services ( )	128,216.36
Contractor's Name & Address: Messrs Katchey Company Ltd, 28632 Roadside Drive Suite 230 Agoura Hills, California, 91301, USA	**Notification of Award & Date**			January 23, 2024
	Acceptance Letter & Date			Not sighted
No. Of Bids Received: Four (4)	**Date of Contract Performance**			Not sighted
	Date of Contract Agreement:			Not sighted
Location of Goods, Works or Service:	ACE-SPED, University of Nigeria, Nsukka.			
TOPIC	**COMMENTS & FINDINGS:**			
PRFOCUREMENT AND CONTRCTING				
Contract Package (Items & Quantity	Supply of Laboratory Equipment: Back scattered Electrons Analytical Equipment			
	Various items			
Contract Type {Goods, Works (S&L) Services}	Good			
Procurement Method (ICB, LIB, NCB, SHOPPING-RFQ/RFT)	RFQ			
Prequalification (Yes/No)	No			
Single Stage/Two Stage	Single Stage			
Domestic Preference (Yes/No)	No			
Bank Review (PRIOR, POST, SOL)	Prior			
COSTS				

USD Equivalent	128,216.36			
Exchange Rate/Date	USD 1300.00 (November, 2023).			
Price of Lowest Evaluated Bidder (N)				
Contract Value at Award (N)	USD128,216.36			
Contingencies in PAD	N/A			
Final Contract Price	USD128,216.36*)*			
TIME (DATE)				
General Procurement Notice (GPN)	Not used – approval obtained from BPP to use selection			
Request for Proposal (RFP)	Not Applicable			
Invitation for Prequalification	Not Applicable			
Invitation for Bids	November 24, 2023			
Submission of Bids	December 22, 2024			
Contract Award Signature	January 23, 2024			
Date of Contract Performance	Contract Performance – Not sighted			
Completion Period offered to the Contractor.	Four (4) weeks			
Date of Contract Completion	Completion –			
CONTRACT ADMINISTRATION:				
Changes to Contract	**Description**	**Date**	**Price Impact**	
	None	Not Applicable	Not Applicable	
Final Payment	**Description**	**Date of Invoice**	**Date of Payment**	
	Supply of Laboratory Equipment: Back scattered Electrons Analytical Equipment – Lot 3	Not due	Not due (goods not delivered yet)	
Total Payment	Not yet due (goods not delivered yet)			
DISBURSEMENT				
Disbursement Method (Direct, SOE, Special Account)	Direct			
Percentage of Bank Financing (%)	2.14%			
Disbursements: Amount & Date:	No payment made as at the date of audit (as stated by the procurement officer)			
DELIVERABLES:				
Contract Package	**Reference/ Description**	**Quantity/% Completed**	**Date Delivered/ Completed**	**Remarks** *(Note any Discrepancies from Contract)*

UNN/ACESPED/GDS/05/2023/7-9 - LOT 3	Supply of Laboratory Equipment: Back scattered Electrons Analytical Equipment.	0%	Not yet delivered	None

Start date of Contract Performance	Not sighted
Completion Period offered by the Contractor.	Three (3) weeks.
Date of Contract Completion	Not sighted

AFRICA CENTRE OF EXCELLENCE CENTRE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA

WORKS

PROCUREMENT DURATION FORM

Contract No: UNN/ACESPED/GDS/01/2024/1-4/ LOT 1
Contract Name: Contract Name & Number:

Supply of Laboratory Equipment:XRF Spectrometer-AIR & Helium including installation/commissioning/end user training (Lot 1) to ACESPED Building

Date General Procurement Notice (GPN): Not Used

Bid Validity Period: 180 Days

S/No.	STEPS	DURATION (DAYS)		
		Actual Date	**Between Events**	**Overall** (No of Days)
1	**Prequalification documents received by Bank**	Not Applicable	0	0
2	**Bank's No Objection**	Not Applicable	0	0
3	**Invitation for Prequalification issued**	Not Applicable	0	0
4	**Submission of Prequalification applications**	Not Applicable	0	0
5	**PQ Evaluation Report received by Bank**	Not Applicable	0	0
6	**Bank's No Objection**	Not Applicable	0	0
7	**Bid documents received by Bank**	Not Applicable	0	0
8	**Bank's No Objection/BPP No Objection**	None	0	0
9	**Invitation for Bids issued**	November 24, 2023	0	0
10	**Submission of bids**	December 22, 2024	28	28
11	**Bid Evaluation Report preparation (financial)**	January 2024	0	0
12	**Request for Clarification**	Not Applicable	0	0
13	**Bank's No Objection**	Not Applicable	0	0
14	**Contract Award Notice**	January 23, 2024	32	32
15	**Contract Signed**	Not Sighted	0	0
	TOTAL DAYS		DAYS	**60 DAYS**

AFRICA CENTRE OF EXCELLENCE CENTRE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA

GOOD

CHECK LIST

2. AWARD OF CONTRACT FOR LANDSCAPING AND XTERNAL WORKS TO ACESPED CORE ADMINISTRATIIVE BUILDING PREMISES

LOAN/CREDIT NO. 6510-NG	**REVIEW DATE:** FEBRUARY 12, 2025			
CONTRACT DATA				
Contract Name & Number: Award of contract for landscaping and external works to ACESPED core administrative building premises	**Type of Contract: Lump Sum**			**Contract Amount: N**
	Goods ( )	Works (**X**)	Services ( )	116,572,247.50
Contractor's Name & Address: Messrs Faxco Nigeria Limited, No. 12 Kamba Street, Wuse Zone 2, Abuja.	**Notification of Award & Date**			August 14, 2024
	Acceptance Letter & Date			August 23, 2024
No. Of Bids Received: Three (3)	**Date of Contract Performance**			Not sighted
	Date of Contract Agreement:			Not sighted
Location of Goods, Works or Service:	ACE-SPED, University of Nigeria, Nsukka.			
TOPIC	**COMMENTS & FINDINGS:**			
PRFOCUREMENT AND CONTRCTING				
Contract Package (Items & Quantity	Award of contract for landscaping and external works to ACESPED core administrative building premises			
	Various items			
Contract Type {Goods, Works (S&L) Services}	Works			
Procurement Method (ICB, LIB, NCB, SHOPPING-RFQ/RFT)	RFQ			
Prequalification (Yes/No)	No			
Single Stage/Two Stage	Single Stage			
Domestic Preference (Yes/No)	No			
Bank Review (PRIOR, POST, SOL)	Prior			
COSTS				
USD Equivalent	73,325.10			

Exchange Rate/Date	USD 1,589.80 (August 14, 2024).			
Price of Lowest Evaluated Bidder (N)	116,572,247.50			
Contract Value at Award (N)	116,572,247.50			
Contingencies in PAD	N/A			
Final Contract Price	116,572,247.50 (gross)			
TIME (DATE)				
General Procurement Notice (GPN)	Not used			
Request for Proposal (RFP)	Not Applicable			
Invitation for Prequalification	Not Applicable			
Invitation for Bids	July 12, 2024			
Submission of Bids	August 2, 2024			
Contract Award Signature	August 14, 2024			
Start date of Contract Performance	Contract Performance – Not sighted			
Completion Period offered by the Contractor.	Three (3) weeks			
Date of Contract Completion	Completion – Not sighted			
CONTRACT ADMINISTRATION:				
Changes to Contract	**Description**	**Date**	**Price Impact**	
	None	Not Applicable	Not Applicable	
Final Payment	**Description**	**Date of Invoice**	**Date of Payment**	
	Award of contract for landscaping and external works to ACESPED core administrative building premises	Not sighted	September 6, 2024	
Total Payment	N100,834,994.09			
DISBURSEMENT				
Disbursement Method (Direct, SOE, Special Account)	Direct			
Percentage of Bank Financing (%)	1.22%			
Disbursements: Amount & Date:	Net N100,834,994.09 with PV/2024/UNN-1/000000370 of September 6, 2024			
DELIVERABLES:				
Contract Package	**Reference/ Description**	**Quantity/% Completed**	**Date Delivered/ Completed**	**Remarks** *(Note any Discrepancies from Contract)*
	Award of	100%	Not sighted	None

	contract for landscaping and external works to ACESPED core administrative building premises ACESPED Centre			

AFRICA CENTRE OF EXCELLENCE CENTRE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA

WORKS

PROCUREMENT DURATION FORM

Contract No: SEE INVENTORY
Contract Name: Award of contract for landscaping and external works to ACESPED core administrative building premises ACESPED Centre

Date General Procurement Notice (GPN): Not Used

Bid Validity Period: Not Stated

S/No.	STEPS	DURATION (DAYS)		
		Actual Date	**Between Events**	**Overall** (No of Days)
1	**Prequalification documents received by Bank**	Not Applicable	0	0
2	**Bank's No Objection**	Not Applicable	0	0
3	**Invitation for Prequalification issued**	Not Applicable	0	0
4	**Submission of Prequalification applications**	Not Applicable	0	0
5	**PQ Evaluation Report received by Bank**	Not Applicable	0	0
6	**Bank's No Objection**	Not Applicable	0	0
7	**Bid documents received by Bank**	Not Applicable	0	0
8	**Bank's No Objection/BPP No Objection**	None	0	0
9	**Invitation for Bids issued**	July 12, 2024	0	0
10	**Submission of bids**	August 2, 2024	21	21
11	**Bid Evaluation Report preparation (financial)**	August 10, 2024	8	8
12	**Request for Clarification**	Not Applicable	0	0
13	**Bank's No Objection**	Not Applicable	0	0
14	**Contract Award Notice**	August 14, 2024	4	4
15	**Contract Signed**	Not sighted	0	0
	TOTAL DAYS		DAYS	**25 DAYS**

AFRICA CENTRE OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA, ENUGU STATE

WORKS

CHECK LIST

3. Landscaping and External Works to ACE-SPED Core Administrative Building Premises (Perimeter Fencing Lot 1) at University of Nigeria, Nsukka Campus

LOAN/CREDIT NO.6510-NG	**REVIEW DATE:** FEBRUARY 12, 2025			
CONTRACT DATA				
Contract Name: Landscaping and External Works to ACE-SPED Core Administrative Building Premises (Perimeter Fencing Lot 1) at University of Nigeria, Nsukka Campus **Contract Number:** VC/PPU/SP/18/103	**Type of Contract: Lump Sum**			**Contract Amount:** N
	Goods ( )	Works **(X)**	Services ( )	49,257,790.00
Contractor's Name: Messrs. Bethlyke Nigeria Limited **Contractor's Address:** 79 Ogui Road, Enugu, Enugu State.	**Notification of Award & Date**			August 14, 2024
	Acceptance Letter & Date			August 23, 2024
No. Of Bids Received: Three (3)	**Start Date of Contract Performance:**			Not Sighted
	Date of Contract Agreement:			Not Sighted
Location of Goods, Works or Service:	ACE-SPED – University of Nigeria, Nsukka, Enugu State			
TOPIC	**COMMENTS & FINDINGS:**			
PRFOCUREMENT AND CONTRCTING				
Contract Package (Items & Quantity	Item: Landscaping and External Works to ACE-SPED Core administrative Building Premises (Perimeter Fencing Lot 1) at University of Nigeria, Nsukka Campus			
	- Quantity: Bill of Quantities			
Contract Type {Goods, Works (S&L) Services}	Works			
Procurement Method (ICB, LIB, NCB, SHOPPING-RFQ/RFT)	RFQ			
Prequalification (Yes/No)	No			
Single Stage/Two Stage	Single Stage			
Domestic Preference (Yes/No)	No			
Bank Review (PRIOR, POST, SOL)	Prior			
COSTS				

USD Equivalent	$30,983.64
Exchange Rate/Date	USD 1,589.80 (As at August 14, 2024).
Price of Lowest Evaluated Bidder (N)	49,257,790.00
Contract Value at Award (N)	49,257,790.00
Contingencies in PAD	N/A
Final Contract Price (N)	49,257,790.00
TIME (DATE)	
General Procurement Notice (GPN)	Not Applicable
Request for Proposal (RFP)	Not Applicable
Invitation for Prequalification	Not Applicable
Invitation for Bids	July 12, 2024
Submission of Bids/Quotation	August 2, 2024
Contract Award Signature	August 14, 2024
Start Date of Contract Performance	Not Sighted
Completion Period Offered by the Contractor	Not stated
Date of Contract completion	August 27, 2024

CONTRACT ADMINISTRATION:			
Changes to Contract	**Description**	**Date**	**Price Impact**
	None	Not Applicable	Not Applicable
Final Payment	**Description**	**Date of Invoice**	**Date of Payment**
	Payment for Landscaping and External Works at ACE-SPED Administrative	August 27, 2024	September 2, 2024.
Total Payment	N49,257,790.00 (Gross)		

DISBURSEMENT	
Disbursement Method (Direct, SOE, Special Account)	Direct
Percentage of Bank Financing (%)	0.52%
Disbursements: Amount & Date	N42,607,988.35 Net - Payment for Landscaping and External Works at ACE-SPED Administrative through a Payment Voucher No. PV/2024/UNN-1/000000334 of September 2, 2024.

DELIVERABLES:				
Contract Package	**Reference/ Description**	**Quantity/% Completed**	**Date Delivered/ Completed**	**Remarks** *(Note any Discrepancies from Contract)*
VC/PPU/SP/18/103	Landscaping and External	100%	August 27, 2024	None

	Works to ACE-SPED Core Administrative Building Premises (Perimeter Fencing Lot 1) at University of Nigeria, Nsukka Campus			

AFRICA CENTRE OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA, ENUGU STATE

WORKS

PROCUREMENT DURATION FORM

Contract No: VC/PPU/SP/18/103
Contract Name Landscaping and External Works to ACE-SPED Core Administrative Building Premises (Perimeter Fencing Lot 1) at University of Nigeria, Nsukka Campus
Date General Procurement Notice (GPN): Not Used
Bid Validity Period: Not Sighted

S/No.	STEPS	DURATION (DAYS)		
		Actual Date	Between Events	Overall (No of Days)
1	**Prequalification documents received by Bank**	Not Applicable	0	0
2	**Bank's No Objection**	Not Applicable	0	0
3	**Invitation for Prequalification issued**	Not Applicable	0	0
4	**Submission of Prequalification applications**	Not Applicable	0	0
5	**PQ Evaluation Report received by Bank**	Not Applicable	0	0
6	**Bank's No Objection**	Not Applicable	0	0
7	**Bid documents received by Bank**	Not Applicable	0	0
8	**Bank's No Objection/BPP No Objection**	None	0	0
9	**Invitation for Bids issued**	July 12, 2024	0	0
10	**Submission of bids**	August 2, 2024	26	26
11	**Bid Evaluation Report preparation (financial)**	August 7, 2024	5	5
12	**Request for Clarification**	Not Applicable	0	0
13	**Bank's No Objection**	Not Applicable	0	0
14	**Contract Award Notice**	August 14, 2024	7	7
15	**Contract Signed**	Not Sighted	0	0
	TOTAL DAYS		DAYS	**38 DAYS**

AFRICA CENTRE OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA, ENUGU STATE

WORKS

CHECK LIST

1. Landscaping and External Works to ACE-SPED Core Administrative Building Premises (Drains, Kerbs and Grassing) Lot 3 at University of Nigeria, Nsukka Campus

LOAN/CREDIT NO.6510-NG	**REVIEW DATE:** FEBRUARY 12, 2025			
CONTRACT DATA				
Contract Name: Landscaping and external Works to ACE-SPED Core Administrative Building Premises (Drains, Kerbs and Grassing) Lot 3 at University of Nigeria, Nsukka Campus **Contract Number:** VC/PPU/SP/18/104	**Type of Contract: Lump Sum**			**Contract Amount:** N
	Goods ( )	Works **(X)**	Services ( )	30,556,552.50
Contractor's Name: Messrs. MCO Contractors **Contractor's Address:** 12 Nza Street, Independence Layout, Enugu, Enugu State.	**Notification of Award & Date**			August 14, 2024
	Acceptance Letter & Date			August 23, 2024
No. Of Bids Received: Three (3)	**Start Date of Contract Performance:**			Not Sighted
	Date of Contract Agreement:			Not Sighted
Location of Goods, Works or Service:	ACE-SPED – University of Nigeria, Nsukka, Enugu State			
TOPIC	**COMMENTS & FINDINGS:**			
PRFOCUREMENT AND CONTRCTING				
Contract Package (Items & Quantity	Item: Landscaping and External Works to ACE-SPED Core Administrative Building Premises (Drains, Kerbs and Grassing) Lot 3 at University of Nigeria, Nsukka Campus			
	- Quantity: Bill of Quantities			
Contract Type {Goods, Works (S&L) Services}	Works			
Procurement Method (ICB, LIB, NCB, SHOPPING-RFQ/RFT)	RFQ			
Prequalification (Yes/No)	No			
Single Stage/Two Stage	Single Stage			
Domestic Preference (Yes/No)	No			
Bank Review (PRIOR, POST, SOL)	Prior			
COSTS				
USD Equivalent	$19,220.38			

Exchange Rate/Date	USD 1,589.80 (As at August 14, 2024).			
Price of Lowest Evaluated Bidder (N)	30,556,552.50			
Contract Value at Award (N)	30,556,552.50			
Contingencies in PAD	N/A			
Final Contract Price (N)	30,556,552.50			
TIME (DATE)				
General Procurement Notice (GPN)	Not Applicable			
Request for Proposal (RFP)	Not Applicable			
Invitation for Prequalification	Not Applicable			
Invitation for Bids	July 12, 2024			
Submission of Bids/Quotation	August 2, 2024			
Contract Award Signature	August 14, 2024			
Start Date of Contract Performance	Not Sighted			
Completion Period Offered by the Contractor	Not stated			
Date of Contract completion	August 27, 2024			
CONTRACT ADMINISTRATION:				
Changes to Contract	**Description**	**Date**	**Price Impact**	
	None	Not Applicable	Not Applicable	
Final Payment	**Description**	**Date of Invoice**	**Date of Payment**	
	Payment for Landscaping and External Works at ACE-SPED	August 27, 2024	September 2, 2024.	
Total Payment	N30,556,552.50 (Gross)			
DISBURSEMENT				
Disbursement Method (Direct, SOE, Special Account)	Direct			
Percentage of Bank Financing (%)	0.32%			
Disbursements: Amount & Date	N26,431,417.91 Net - Payment for Landscaping and External Works at ACE-SPED through a Payment Voucher No. PV/2024/UNN-1/000000395 of September 2, 2024.			
DELIVERABLES:				
Contract Package	**Reference/ Description**	**Quantity/% Completed**	**Date Delivered/ Completed**	**Remarks** *(Note any Discrepancies from Contract)*
VC/PPU/SP/18/104	Landscaping and External Works to ACE-	100%	August 27, 2024	None

	SPED Core Administrative Building Premises (Drains, Kerbs and Grassing) Lot 3 at University of Nigeria, Nsukka Campus			

AFRICA CENTRE OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA, ENUGU STATE

WORKS

PROCUREMENT DURATION FORM

Contract No: VC/PPU/SP/18/104
Contract Name Landscaping and External Works to ACE-SPED Core Administrative Building Premises (Drains, Kerbs and Grassing) Lot 3 at University of Nigeria, Nsukka Campus
Date General Procurement Notice (GPN): Not Used
Bid Validity Period: Not Sighted

S/No.	STEPS	DURATION (DAYS)		
		Actual Date	Between Events	Overall (No of Days)
1	**Prequalification documents received by Bank**	Not Applicable	0	0
2	**Bank's No Objection**	Not Applicable	0	0
3	**Invitation for Prequalification issued**	Not Applicable	0	0
4	**Submission of Prequalification applications**	Not Applicable	0	0
5	**PQ Evaluation Report received by Bank**	Not Applicable	0	0
6	**Bank's No Objection**	Not Applicable	0	0
7	**Bid documents received by Bank**	Not Applicable	0	0
8	**Bank's No Objection/BPP No Objection**	None	0	0
9	**Invitation for Bids issued**	July 12, 2024	0	0
10	**Submission of bids**	August 2, 2024	26	26
11	**Bid Evaluation Report preparation (financial)**	August 7, 2024	5	5
12	**Request for Clarification**	Not Applicable	0	0
13	**Bank's No Objection**	Not Applicable	0	0
14	**Contract Award Notice**	August 14, 2024	7	7
15	**Contract Signed**	Not Sighted	0	0
	TOTAL DAYS		DAYS	**38 DAYS**

AFRICA CENTRE OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA, ENUGU STATE

WORKS

CHECK LIST

5 Proposed Construction of Generator House and Procurement of 200KVA Generator for ACE-SPED Core Building University of Nigeria Nsukka Campus

LOAN/CREDIT NO.6510-NG	**REVIEW DATE:** FEBRUARY 12, 2025			
CONTRACT DATA				
Contract Name: Proposed Construction of Generator House and Procurement of 200KVA Generator for ACE-SPED Core Building University of Nigeria, Nsukka Campus **Contract Number:** VC/PPU/SP/18/104	**Type of Contract: Lump Sum**			**Contract Amount:** N
	Goods ( )	Works **(X)**	Services ( )	60,381,184.80
Contractor's Name: Messrs. Fraemmanon Investment Ltd. **Contractor's Address:** 3rd Floor, 4 Ogui Road, Enugu, Enugu State.	**Notification of Award & Date**			October 30, 2024
	Acceptance Letter & Date			October 31, 2024
No. Of Bids Received: Three (3)	**Start Date of Contract Performance:**			Not Sighted
	Date of Contract Agreement:			Not Sighted
Location of Goods, Works or Service:	ACE-SPED – University of Nigeria, Nsukka, Enugu State			
TOPIC	**COMMENTS & FINDINGS:**			
PRFOCUREMENT AND CONTRCTING				
Contract Package (Items & Quantity	Item: Proposed Construction of Generator House and Procurement of 200KVA Generator for ACE-SPED Core Building University of Nigeria, Nsukka Campus			
	- Quantity: One (1)			
Contract Type {Goods, Works (S&L) Services}	Works			
Procurement Method (ICB, LIB, NCB, SHOPPING-RFQ/RFT)	RFQ			
Prequalification (Yes/No)	No			
Single Stage/Two Stage	Single Stage			
Domestic Preference (Yes/No)	No			
Bank Review (PRIOR, POST, SOL)	Prior			
COSTS				

USD Equivalent	$35,160.53
Exchange Rate/Date	USD 1,717.30 (As at October 30, 2024).
Price of Lowest Evaluated Bidder (N)	60,381,184.80
Contract Value at Award (N)	60,381,184.80
Contingencies in PAD	N/A
Final Contract Price (N)	60,381,184.80
TIME (DATE)	
General Procurement Notice (GPN)	Not Applicable
Request for Proposal (RFP)	Not Applicable
Invitation for Prequalification	Not Applicable
Invitation for Bids	September 3, 2024
Submission of Bids/Quotation	September 29, 2024
Contract Award Signature	October 30, 2024
Start Date of Contract Performance	Not Sighted
Completion Period Offered by the Contractor	Not stated
Date of Contract completion	November 8, 2024

CONTRACT ADMINISTRATION:			
Changes to Contract	**Description**	**Date**	**Price Impact**
	None	Not Applicable	Not Applicable
Final Payment	**Description**	**Date of Invoice**	**Date of Payment**
	PMT for construction of Generator House and Procurement of 200KV	November 8, 2024	November 11, 2024
Total Payment	N60,381,184.80 (Gross)		

DISBURSEMENT	
Disbursement Method (Direct, SOE, Special Account)	Direct
Percentage of Bank Financing (%)	0.59%
Disbursements: Amount & Date	N52,229,724.85Net – PMT for construction of Generator House and Procurement of 200KV through a Payment Voucher No. PV/2024/UNN-1/000000463 of November 11, 2024

DELIVERABLES:				
Contract Package	**Reference/ Description**	**Quantity/% Completed**	**Date Delivered/ Completed**	**Remarks** *(Note any Discrepancies from Contract)*
VC/PPU/SP/18/104	Proposed Construction of Generator	100%	November 8, 2024	None

	House and Procurement of 200KVA Generator for ACE-SPED Core Building University of Nigeria, Nsukka Campus			

AFRICA CENTRE OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACESPED)

UNIVERSITY OF NIGERIA NSUKKA, ENUGU STATE

WORKS

PROCUREMENT DURATION FORM

Contract No: VC/PPU/SP/18/104
Contract Name Proposed Construction of Generator House and Procurement of 200KVA Generator for ACE-SPED Core Building University of Nigeria, Nsukka Campus
Date General Procurement Notice (GPN): Not Used
Bid Validity Period: Not Sighted

S/No.	STEPS	DURATION (DAYS)		
		Actual Date	Between Events	Overall (No of Days)
1	**Prequalification documents received by Bank**	Not Applicable	0	0
2	**Bank's No Objection**	Not Applicable	0	0
3	**Invitation for Prequalification issued**	Not Applicable	0	0
4	**Submission of Prequalification applications**	Not Applicable	0	0
5	**PQ Evaluation Report received by Bank**	Not Applicable	0	0
6	**Bank's No Objection**	Not Applicable	0	0
7	**Bid documents received by Bank**	Not Applicable	0	0
8	**Bank's No Objection/BPP No Objection**	None	0	0
9	**Invitation for Bids issued**	September 3, 2024	0	0
10	**Submission of bids**	September 29, 2024	26	26
11	**Bid Evaluation Report preparation (financial)**	October 27, 2024	28	28
12	**Request for Clarification**	Not Applicable	0	0
13	**Bank's No Objection**	Not Applicable	0	0
14	**Contract Award Notice**	October 30, 2024	3	3
15	**Contract Signed**	Not Sighted	0	0
	TOTAL DAYS		DAYS	**57 DAYS**

AFRICA CENTRE OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACE-SPED)

UNIVERSITY OF NIGERIA, NSUKKA

WORKS

CHECK LIST

6. DRILLING OF BOREHOLE FOR WATER RETICULATION AT THE CORE BUILDING ACE-SPED CENTRE, UNIVERSITY OF NIGERIA NSUKKA CAMPUS.

LOAN/CREDIT NO.6510-NG	**REVIEW DATE:** FEBRUARY 12, 2025			
CONTRACT DATA				
Contract Name: Drilling of borehole for water reticulation at the core building ace-sped Centre, University of Nigeria Nsukka campus. **Contract Number:**	**Type of Contract: Lump Sum**			**Contract Amount: N**
	Goods ()	Work **(X)**	Services ()	19,984,575.00
Contractor's Name: Messrs. Faxco Nigeria Limited. **Contractor's Address:**	**Notification of Award & Date**			June 3, 2024
	Acceptance Letter & Date			Not Sighted
No. Of Bids Received: Three (3)	**Start Date of Contract Performance:**			Not Sighted
	Date of Contract Agreement:			Not Sighted
Location of Goods, Works or Service:	ACE-SPED, University of Nigeria, Nsukka.			
TOPIC	**COMMENTS & FINDINGS:**			
PRFOCUREMENT AND CONTRCTING				
Contract Package (Items & Quantity	Contract package: Drilling of borehole for water reticulation at the core building ace-sped Centre, University of Nigeria Nsukka campus.			
	Quantities: One (1)			
Contract Type {Goods, Works (S&L) Services}	WORKS			
Procurement Method (ICB, LIB, NCB, SHOPPING-RFQ/RFT)	RFQ			
Prequalification (Yes/No)	No			
Single Stage/Two Stage	Single stage			
Domestic Preference (Yes/No)	No			
Bank Review (PRIOR, POST, SOL)	Post			
COSTS				
USD Equivalent	USD 13,440.42			
Exchange Rate/Date	N1,486.90 (as at June 3, 2024)			

Price of Lowest Evaluated Bidder (N)	19,984,575.00			
Contract Value at Award (N)	19,984,575.00			
Contingencies in PAD	None			
Final Contract Price (N)	19,984,575.00 (Gross)			
TIME (DATE)				
General Procurement Notice (GPN)	Not Applicable			
Request for Proposal (RFP)	Not Applicable			
Invitation for Prequalification	Not Applicable			
Invitation for Bids/Quotation	April 30, 2024			
Submission of Bids/Quotation	May 21, 2024			
Contract Award Signature	June 3, 2024			
Start Date of Contract Performance	Not Sighted			
Completion Period Offered by the Contractor	Eight (8) weeks			
Date of Contract Completion	June 6, 2024.			
CONTRACT ADMINISTRATION:				
Changes to Contract	**Description**	**Date**	**Price Impact**	
	None	None	None	
Final Payment	**Description**	**Date of Invoice**	**Date of Payment**	
	Drilling of borehole for water reticulation at the core building ace-sped Centre, University of Nigeria Nsukka campus.	June 6, 2024.	June 8, 2024.	
Total Payment (N)	16,754,840.55 (Net)			
DISBURSEMENT				
Disbursement Method (Direct, SOE, Special Account)	Direct			
Percentage of Bank Financing (%)	0.22%			
Disbursements: Amount & Date	16,754,840.55 – being net payment for drilling of borehole for water reticulation at the core building ace-sped Centre, University of Nigeria Nsukka campus through voucher no.: PV/2024/UNN-1/000000285 on June 8, 2024.			
DELIVERABLES:				
Contract Package	**Reference/ Description**	**Quantity/% Completed**	**Date Delivered/ Completed**	**Remarks** *(Note any Discrepancies from Contract)*
	Drilling of borehole for water	100%	June 6, 2024.	None

	reticulation at the core building ace-sped Centre, University of Nigeria Nsukka campus			

AFRICA CENTRE OF EXCELLENCE FOR SUSTAINABLE POWER AND ENERGY DEVELOPMENT (ACE-SPED)

PROCUREMENT DURATION FORM

WORKS

Contract No:

Contract Name: Drilling of borehole for water reticulation at the core building ace-sped Centre, University of Nigeria Nsukka campus

Date General Procurement Notice (GPN): Not Applicable.

Bid Validity Period: Not Sighted.

S/No.	STEPS	DURATION (DAYS)		
		Actual Date	**Between Events**	**Overall** (No of Days)
1	**Prequalification documents received by Bank**	Not Applicable	0	0
2	**Bank's No Objection**	Not Applicable	0	0
3	**Invitation for Prequalification issued**	Not Applicable	0	0
4	**Submission of Prequalification applications**	Not Applicable	0	0
5	**PQ Evaluation Report received by Bank**	Not Applicable	0	0
6	**Bank's No Objection**	Not Applicable	0	0
7	**Bid documents received by Bank**	Not Applicable	0	0
8	**Bank's No Objection/BPP No Objection**	None	0	0
9	**Invitation for Bids issued**	April 30, 2024	0	0
10	**Submission of bids**	May 21, 2024	21	21
11	**Bid Evaluation Report preparation (financial)**	May 23, 2024	2	2
12	**Request for Clarification**	Not Applicable	0	0
13	**Bank's No Objection**	Not Applicable	0	0
14	**Contract Award Notice**	June 3, 2024	11	11
15	**Contract Signed**	Not Sighted	0	0
	TOTAL DAYS		DAYS	**34 DAYS**

APPENDIX IV

EXIT MEETING SHEET

UNN – ACESPED

ISSUES AT EXIT MEETING – WITH CENTRE RESPONSES

S/NO	ISSUES RECORDED/CLAUSES	CLAUSE	NATURE OF INFRACTION	CENTRE RESPONSE	REMARK 58.5(a & b); 58.6(a&b); 58.7
1	Not in the Procurement Plan	18(a-g)			
2	Debriefing	19(e)	The unsuccessful bidders were not debriefed.	Used telephone debriefing	
3	Invitation to Bid	25.2(ii)	Some RFQ were used where they should not)	ii. Initial estimate was less than 20million but at collection it turned out to be more than that. Institutional procedures were followed.	The Centre should ensure that such does not occur going forward.
4	Mandatory Compliances	16(6)b			
5	Bids after deadline	27.5			
6	Bid opening register	30(d)			
7	Collusive Practice	58.4(a)			
8	Coercion and unlawful influence *(Directly, indirectly or attempting to influence in any manner the procurement process)*	58.4(b & c)			
9	Contract Splitting	58.4(d)			
10	Bid Rigging	58.4(e); 58.10(a & b)			
11	Competition, transparency - compromised	24			
12	Observers	19(b)			
13	Requested Document not	54.4(h)			

	provided				
14	Non-remittance of Taxes	40* (FIRS establishment) Act 2007			
15	Direct Procurement	42			
16	Expression of Interest	44			
17	Request for Quotation	41			
18	Request for Proposal	45			
19	Bid Validity Period	29			
20	Procurement Planning Committee	21			
21	Tenders Board	22			

APPENDIX V

PROCUREMENT PLAN

PROCUREMENT PLAN – GOODS

Country: Nigeria
Program: ACE SPED
Date: November 09, 2024
Applicable Period: January - December 2024
Project ID:
Implementing Agency: University of Nigeria, Nsukka

		BASIC DATA						Draft Bid Documents, including specs and quantities, draft SPN		Spec Proc Notice Advert	Bidding Period		Bid Evaluation			Contract Finalization				Contract Implementation		
Description*	**Package Number**	**Lot Number**	**Estimated Amount in US $**	**Procurement Method**	**Pre-or Post Qualification**	**Prior or Post Review**	**Plan vs. Actual**	**Prep & Submission by Ex Agency**	**No-objection Date**	**On-line UNDB Gateway Nat Press**	**Bid Invitation Date**	**Bid Closing-Opening**	**Submission Bid Eval Rpt**	**No-objection Date**	**Plan vs. Actual**	**Contract Amount in US$**	**Date Contract Award**	**Date Contract Advert**	**Date Contract Signature**	**Opening of Let of Credit**	**Arrival of Goods**	**Inspection Final Acceptance**
Norm Duration of Proc Steps					If Prequalification		Plan	4 - 7 wks	1 - 1.5 wks	1.5 - 2 wks	6 to	12 wks	1.5 - 3 wks	1 - 1.5 wks	Plan		1 wk		1.5-3 wks			
					add 7-13 wks		Actual								Actual							
List of Contracts																						
Visual Learning Equipments, incl. video conferencing and webinars.	UNN/ACESPED/GDS/05/2023	1	50,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	50,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	12/02/2024
R & D equipment/materials for fabrication	UNN/ACESPED/GDS/05/2023	2	15,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	15,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
Procurement of Project Vehicles	UNN/ACESPED/GDS/05/2023	4	67,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	67,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	26/06/2024
							Actual								Actual							
Equipments for Upgrading of UNN internet network (Lionet) for ACE-SPED facilities	UNN/ACESPED/GDS/05/2023	5	150,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	150,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
Equipment for ACESPED fabrication workshop	UNN/ACESPED/GDS/05/2023	6	250,000.00	NCB	Post	Post Review	Plan	17/02/2024	24/02/2024	06/03/2024	06/03/2024	06/04/2024	20/04/2024	N/A	Plan	250,000.00	01/05/2024	15/05/2024	15/05/2024	N/A	16/10/2024	16/10/2024
							Actual								Actual							
Equipment for renewable energy laboratory	UNN/ACESPED/GDS/05/2023	7	190,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	190,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	16/06/2024
							Actual								Actual							
Equipment for advanced materials characterization laboratory	UNN/ACESPED/GDS/05/2023	8	340,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	340,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	16/06/2024
							Actual								Actual							
Equipment for electric power systems laboratory	UNN/ACESPED/GDS/05/2023	9	20,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	20,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	16/06/2024
							Actual								Actual							
Software purchase and development	UNN/ACESPED/GDS/05/2023	10	35,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	35,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
Equipment for laboratory of industrial electronics, power devices and new energy system	UNN/ACESPED/GDS/05/2023	11	117,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	137,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	25/07/2024
							Actual								Actual							
Equipment for high voltage laboratory	UNN/ACESPED/GDS/05/2023	12	150,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	150,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
Equipment for furnishing of 5 nos classrooms	UNN/ACESPED/GDS/05/2023	13	60,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	60,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
							Actual								Actual							
Total Cost			**1,464,000.00**													**1,464,000.00**						

PROCUREMENT PLAN – WORKS

Country: Nigeria
Program: ACE SPED
Date: November 09, 2024
Applicable Period: January - December 2024
Project ID:
Implementing Agency: University of Nigeria, Nsukka

		BASIC DATA						Draft Bid Documents, including specs and quantities, draft SPN		Spec Prse Notice Advert	Bidding Period		Bid Evaluation			Contract Finalization				Contract Implementation		
Description*	**Package Number**	**Lot Number**	**Estimated Amount in US $**	**Procurement Method**	**Pre-or Post Qualification**	**Prior or Post Review**	**Plan vs. Actual**	**Prep & Submission by Ex Agency**	**No-objection Date**	**On-line UNDB Gateway Nat Press**	**Bid Invitation Date**	**Bid Closing-Opening**	**Submission Bid Eval Rpt**	**No-objection Date**	**Plan vs. Actual**	**Contract Amount in US$**	**Date Contract Award**	**Date Contract Advert**	**Date Contract Signature**	**Opening of Let of Credit**	**Arrival of Goods**	**Inspection Final Acceptance**
Norm Duration of Proc Steps					If Prequalification		Plan	4 - 7 wks	1 - 1.5 wks	1.5 - 2 wks	6 to	12 wks	1.5 - 3 wks	1 - 1.5 wks	Plan		1 wk		1.5-3 wks			
					add 7-13 wks		Actual								Actual							
List of Contracts																						
Visual Learning Equipments, incl. video conferencing and webinars.	UNN/ACESPED/GDS/05/2023	1	50,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	50,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	12/02/2024
							Actual								Actual							
R & D equipment/materials for fabrication	UNN/ACESPED/GDS/05/2023	2	15,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	15,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
Procurement of Project Vehicles	UNN/ACESPED/GDS/05/2023	4	67,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	67,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	26/06/2024
							Actual								Actual							
Equipments for Upgrading of UNN internet network (Lionet) for ACE-SPED facilities	UNN/ACESPED/GDS/05/2023	5	150,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	150,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
Equipment for ACESPED fabrication workshop	UNN/ACESPED/GDS/05/2023	6	250,000.00	NCB	Post	Post Review	Plan	17/02/2024	24/02/2024	06/03/2024	06/03/2024	06/04/2024	20/04/2024	N/A	Plan	250,000.00	01/05/2024	15/05/2024	15/05/2024	N/A	16/10/2024	16/10/2024
							Actual								Actual							
Equipment for renewable energy laboratory	UNN/ACESPED/GDS/05/2023	7	190,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	190,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	16/06/2024
							Actual								Actual							
Equipment for advanced materials characterization laboratory	UNN/ACESPED/GDS/05/2023	8	340,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	340,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	16/06/2024
							Actual								Actual							
Equipment for electric power systems laboratory	UNN/ACESPED/GDS/05/2023	9	20,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	20,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	16/06/2024
							Actual								Actual							
Software purchase and development	UNN/ACESPED/GDS/05/2023	10	35,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	35,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
Equipment for laboratory of industrial electronics, power devices and new energy system	UNN/ACESPED/GDS/05/2023	11	117,000.00	Selective Tendering	Post	Post Review	Plan	10/11/2023	17/11/2023	N/A	21/11/2023	19/12/2023	12/01/2024	N/A	Plan	137,000.00	19/01/2024	N/A	26/01/2024	N/A	26/06/2024	25/07/2024
							Actual								Actual							
Equipment for high voltage laboratory	UNN/ACESPED/GDS/05/2023	12	150,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	150,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
Equipment for furnishing of 5 nos classrooms	UNN/ACESPED/GDS/05/2023	13	60,000.00	National Shopping	Post	Post Review	Plan	08/01/2024	N/A	N/A	08/01/2024	16/01/2024	17/01/2024	N/A	Plan	60,000.00	N/A	N/A	23/01/2024	N/A	23/02/2024	25/07/2024
							Actual								Actual							
							Actual								Actual							
Total Cost			**1,464,000.00**													**1,464,000.00**						

PROCUREMENT PLAN - SERVICES

Country/Organisation: Nigeria
Programme: Africa Centre of Excellence for Sustainable Power and Energy Development (ACE-SPED)
Date: November 09, 2024
Applicable Period: January - December 2024
Project ID:
Credit Number:
Implementing Agency: University of Nigeria, Nsukka

								Request for EOI (where required)																									
IDA Credit No.:		Contract Type				Preparation Request for Proposals				Short List			Consultant Proposals		Proposal Evaluation and Negotiation for Projects after May 2002 Technical (T) & Financial (F) and Negotions (N)						Draft Contract		Contract Finalization					Contract Implementation				Remarks
Description*	Selection Method	Lumpsum or Time-Based	Estimated Amount in US$	Prior/Post Review	Plan vs. Actual	Prep & Submission by Ex Ag	No-objection Date	On-line UNDB Gateway Nat Press	Lead-time before shortlist	Submission Date	No-objection Date	Plan vs. Actual	Invitation Date	Submission/ Opening Date	Submission Evaluation Report (T)	No-objection Evaluation Report (T)	Opening Financial Proposals	Preparation Eval Report (T) (F)	Negotiations (N)	Plan vs. Actual	Submission Date	No-objection Date	Contract Amount in US$ '000	Contract Award	Date Contract Advert	Contract Signature	Plan vs. Actual	Mobilization Advance Payment	Draft Report	Final Report	Final Cost	
Norm Duration of Proc Steps					Plan	3 - 6 wks	1 - 2 wks	1 - 1.5 wks	2 wks		1 - 2 wks	Plan	4 to	12 wks	2 - 3 wks	0.5 - 2 wks	2 wks	1 - 2 wks	2 wks	Plan	1 - 2 wks	1 - 2 wks		1 wk		1 - 3 wks	Plan					
Component 1:(Institutional Development)																																	
ACE-SPED Core building complex services	QCBS	Lump Sum	278.00	Prior Review	Plan	20/02/2024	N/A	01/03/2024	12/03/2024	19/03/2024	N/A	Plan	16/04/2024	14/05/2024	28/05/2024	N/A	11/06/2024	21/06/2024	28/06/2024	Plan	04/07/2024	N/A	278.00	12/07/2024	N/A	19/07/2024	Plan	23/07/2024	25/07/2024	30/07/2024	278.17	
												plan																					
ACE-SPED website Services	QCBS	Lump Sum	778.00	Post Review	Plan	20/02/2024	N/A	01/03/2024	12/03/2024	19/03/2024	N/A	Plan	16/04/2024	14/05/2024	28/05/2024	N/A	11/06/2024	21/06/2024	28/06/2024	Plan	04/07/2024	N/A	778.00	12/07/2024	N/A	19/07/2024	Plan	23/07/2024	25/07/2024	30/07/2024	779.14	
					Actual							Actual								Actual							Actual					
Design for fabrication of relevant R & D equipments	QCBS	Lump Sum	5,000.00	Post Review	Plan	20/02/2024	N/A	01/03/2024	12/03/2024	19/03/2024	N/A	Plan	16/04/2024	14/05/2024	28/05/2024	N/A	11/06/2024	21/06/2024	28/06/2024	Plan	04/07/2024	N/A	5,000.00	12/07/2024	N/A	19/07/2024	Plan	23/07/2024	25/07/2024	30/07/2024	5,000.00	
					Actual							Actual								Actual							Actual					
Total Cost			6,056.00																				6,056.00								6,057.31	

APPENDIX V

PICTURES

APPENDIX 5

TERMS OF REFERENCE

3.1 TERMS OF REFERENCE

The Terms of Reference (TOR), the WB Procurement Guideline, the Public Procurement Act 2007 and the Public Service circular relating to the Procurement practice within the University is the guiding framework for the post procurement review. Key procurement processes were considered including:

- Client's Capacity, Adequacy of Staff; Role of Procurement Agents/Consultants; Implementation Arrangements;
- Procurement Plans and Monitoring;
- Advertising;
- Pre/Post-Qualification ;
- Bid Opening;
- Bidding Documents;
- Evaluation and Awards;
- Bid Validity Extensions;
- Signed Contracts;
- Contract Amendments and Change/Variation Orders;
- Actual Contract Payments vs. Contract Award Amount
- Securities (for Bid, Performance, Advances, Insurance, Liability, etc.);
- Contractors' Claims;
- Damages and Penalties for Delays, non-compliance with Functional Guarantees, etc.;
- Payment certificates, payments made (date and value), final price;
- Withdrawals from the Loan/Credit Agreement (date and value);
- Protests from Bidders/Contractors;
- Reasons for Slow Progress of Completion;
- Delays in Payments, Imports, Customs, etc. if any;
- Shipping documents
- Test certificates, quality certificates etc.
- List of deliverables and completion (date, description, quantity, location of goods or works);
- Contractual Disputes and their Resolution;
- Bank Comments/Reviews/Interventions at each stage; Turnaround time and Efficiency;
